

WARM MAGNETS COMMISSIONING POINT 1

HARDWARE COMMISSIONING COORDINATION



NEXT RAT meeting
Thursday 23.08
08:30 in point 1 3595/R-013




Present: Pal Andersen, Ivan Moya, Maria Paz Casas Lino, Pierre Dahlen, Carlos Fernández, Hugues Thiesen.

Excused: Jean-Claude Guillaume, Jacky Mazet

Point 5 – Contact HCC person: María Paz Casas / Ivan Moya

- Maria Paz reported that Jean Claude had confirmed that the works in the DC cables have been completed.
- A small leak in one of the warm magnets was detected. It is planned to be fixed in the afternoon 14th August. (DONE)
- The WELQA is planned to be carried out in the morning 14th August anyway, since the leak did not prevent the test (DONE)
- WIC Magnets is foreseen just after the ELQA, the 14th (DONE)
- The connection of the DC cables to the power converters, deconsignation and start up of the converter is planned for the afternoon 14th (DONE)
- The WIC PC is planned for the morning 15th (DONE)
- The beginning of the PC set-up is planned for the afternoon 15th (DONE)
- The following days, the works will follow the planning below.

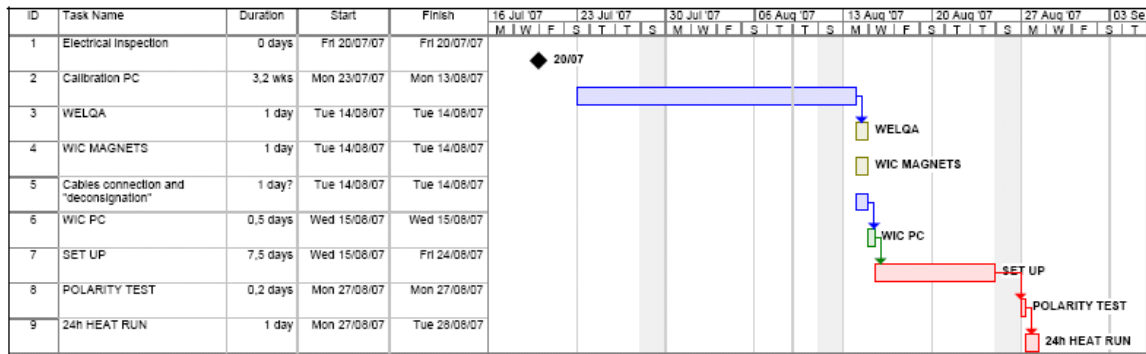

Maria Paz and Ivan Moya for the Hardware Commissioning Coordination
